

— STATEMENT OF WORK

Trellix DLP & Skyhigh SSE

Implementation Plan

Comprehensive Data Protection with Data Discovery

 DURATION

16 Weeks

 COVERAGE

**Endpoint +
Network + Cloud**

 LICENSES

4,500 Users

 TARGET DATE

February 2026

Implementation Roadmap

A comprehensive guide to deploying enterprise-grade data protection across your organization

8 Key Phases

01



Executive Overview

Solution architecture & strategic objectives alignment.

02



Bill of Materials

Complete BOM with SKUs & quantities (4,500 licenses).

03



Scope of Work

Project inclusions, exclusions & key deliverables.

04



Infrastructure

Hardware, network & Skyhigh prerequisites setup.

05



Timeline

16-week phased deployment plan execution.

06



RACI Matrix

Governance & responsibility assignment model.

07



Quality Control

Acceptance criteria & critical success factors.


08



Risk Management

Risk matrix & mitigation strategies.

Solution Overview

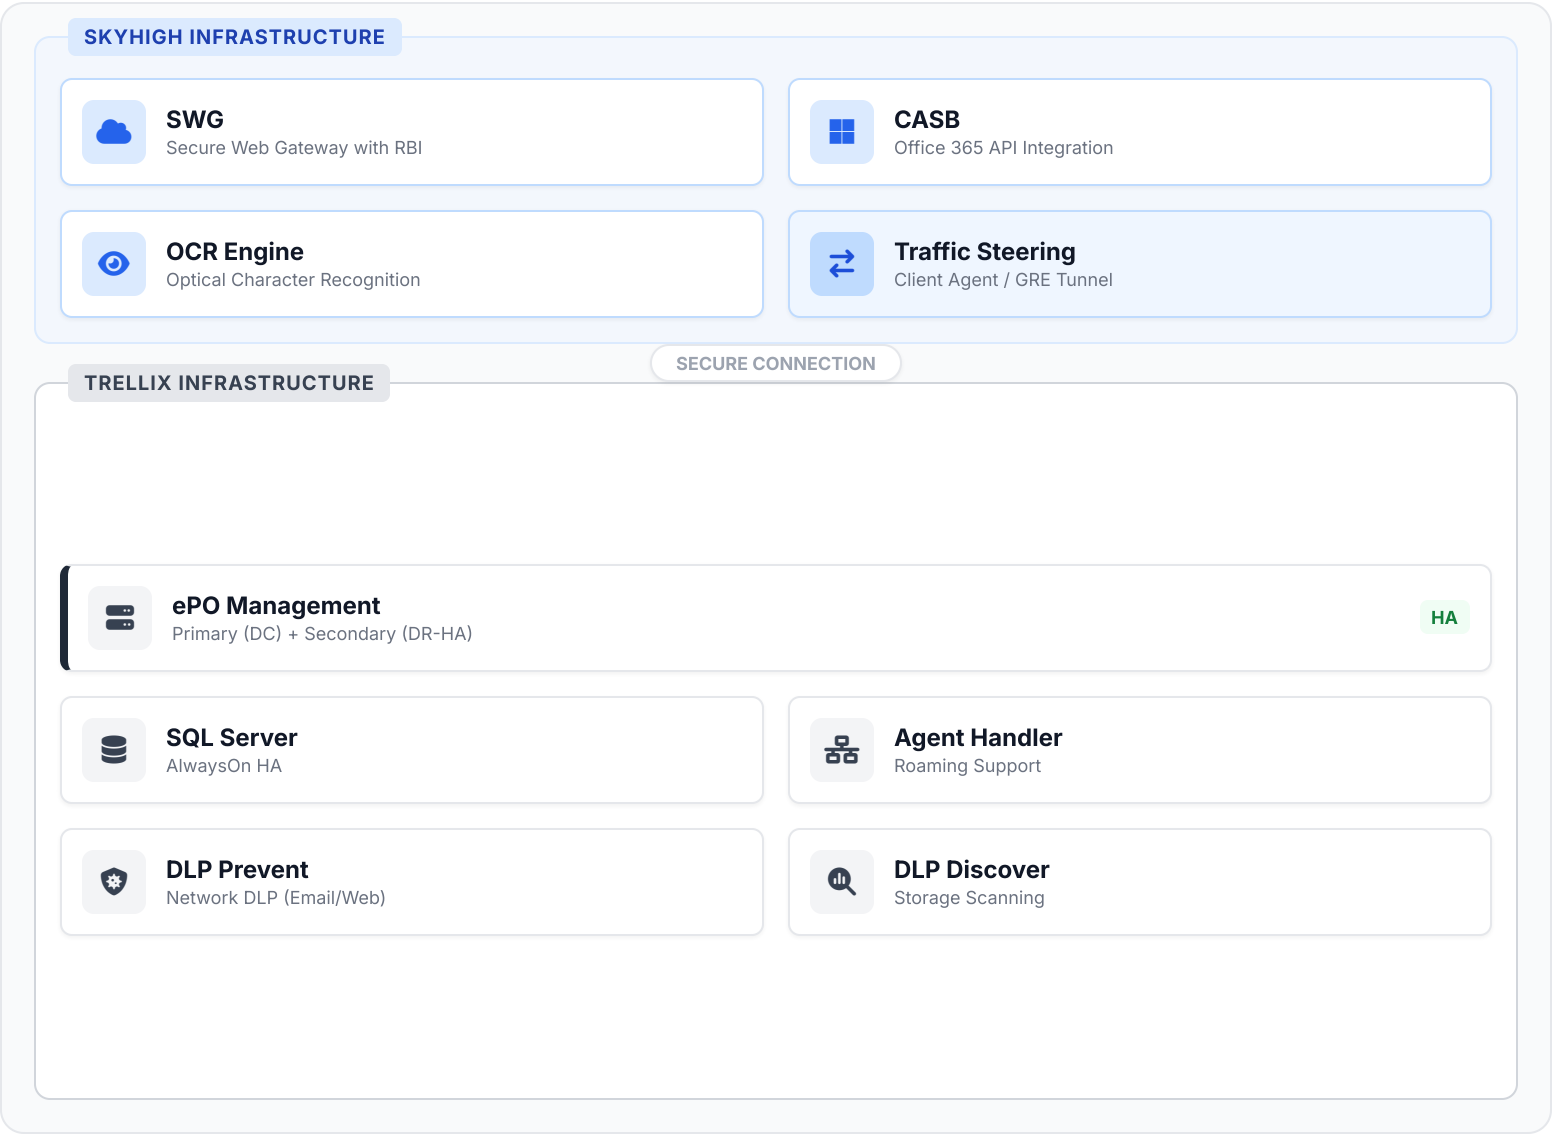

Strategic Objectives

- 1 Prevent Data Exfiltration**
Protect data across endpoint, network, and web channels against unauthorized transfer.
- 2 Enforce Compliance**
Meet industry standards and regulatory requirements for data privacy.
- 3 Secure Hybrid Workforce**
Ensure consistent internet access protection for remote and roaming users.
- 4 Centralized Visibility**
Unified incident management and monitoring through a single pane of glass.
- 5 High Availability**
Robust HA architecture with automatic failover capabilities.
- 6 Data Discovery at Rest**
Locate, identify, and classify sensitive data residing on network storage.

Trellix Components

 Valid Quote

PRODUCT CATEGORY	PRODUCT NAME	SKU	QTY	TERM
Subscription + Support Data Loss Prevention	Data Loss Prevention Suite 1:1TE 1yr Subscription with 1yr Thrive Essential	TDLECE-AA	4,500	3 Years
OCR Module	OCR Scanning for DLPen SW 1:1TE 1yr Subscription with 1yr Thrive Essential	OCRENECE-AT	4,500	3 Years
Professional Services	Solution Services Consultation Voucher Prepaid 12Mo Expire	CONSULT-VOUCHER	131	1 Year

USER LICENSES



4,500

Full Suite Coverage

SUBSCRIPTION TERM



3 Years

Active Support

OCR ACCURACY



90%+

Image Text Extraction

SUPPORT COVERAGE



24x7

Thrive Essential

Skyhigh Components

SSE Platform

PRODUCT CATEGORY	PRODUCT NAME	SKU	QUANTITY / DETAILS	TERM
● Cloud Security	Skyhigh SSE Essential Cloud Proxy Including RBI	UCBECE-AA	4,500 Users	3 Years
● Cloud Security	Secure Edge OCR Optical Character Recognition	OCRECE-AA	4,500 Users	3 Years
● Support	Service Level Adv/Fnd	SL-Adv/Fnd	Y1: Advanced (TAM+Train+24×7) Y2-3: Foundation (24×7)	3 Years
● Cloud Security	CASB for Microsoft O365 Mail / SharePoint / OneDrive	C12ECE-AA	4,500 Users	3 Years
● Services	Professional Services Prepaid	MSH-CUSTCON	5 Days (Year 1)	1 Year
● Cloud Security	Cloud App Isolation AddOn Unmanaged Device Protection	RBIECE-AA	4,500 Users	3 Years
● Network	Dedicated Egress IP Addon	DEIECE-AA	2 IPs	3 Years
● Services	Implementation & Resident Engineer Partner Service	Partner Svc	2 Engineers	3 Years

USER LICENSES

4,500

Full Cloud Coverage

SUBSCRIPTION TERM

3 Years

Active Support

SUPPORT LEVEL

24×7

Advanced + Foundation

RESOURCES

2 Eng

Resident Engineers

Project Scope

 Change orders available for scope modification



In Scope Deliverables

Primary Focus

TRELLIX COMPONENTS

- ✔ **ePO Installation (DC + DR)**
High Availability Setup
- ✔ **SQL HA Setup**
AlwaysOn/Mirroring Configuration
- ✔ **DLP Endpoint & Prevent**
Policies, Deployment & Network DLP
- ✔ **DLP Discover**
Data Classification & Scanning
- ✔ **Agent Handler** - Roaming clients
- ✔ **AD Integration** - User sync
- ✔ **Incident Workflow** - Configuration
- ✔ **HA/DR Testing** - Validation
- ✔ **Training** - Admin & user

SKYHIGH COMPONENTS

- ✔ **Tenant Provisioning**
Cloud setup
- ✔ **Identity Integration**
AD / Azure AD
- ✔ **Traffic Steering**
Agent / GRE tunnel
- ✔ **CASB Policies** - O365 integration
- ✔ **URL Filtering** - Category blocking
- ✔ **Application Control** - Restrictions
- ✔ **Email & Web DLP** - Data protection
- ✔ **Anti-malware** - Threat protection
- ✔ **SIEM Integration** - Log forwarding



Exclusions

Out of Scope

- ✖ **Endpoint Hardware Upgrade**
Existing hardware must meet requirements
- ✖ **Firewall Redesign**
Architecture changes not included
- ✖ **SIEM Licensing**
Customer responsible for platform licenses
- ✖ **ZTNA Functionality**
Zero Trust Network Access not in scope
- ✖ **Custom Scripting**
Custom DLP scripting not included



Note: Additional components can be added via change order. Please contact your account manager for scope modifications.

Infrastructure Requirements

Hardware specifications for Trellix Components

On-Premises Infrastructure

COMPONENT	SPECIFICATIONS		QTY	COMMENTS
 ePO App Server Management Console	OS	Win Server 2025/2022	2	1 at DC and 1 at DR in HA Configuration
	CPU	Intel Xeon 2.2GHz (8 Cores)		
 Database Server SQL Backend	OS	Win Server 2025/2022	2	1 at DC and 1 at DR in HA (AlwaysOn)
	CPU	8 Cores		
 DLP Prevent Network DLP	HYP	VMware 5.5+ / Hyper-V	2	1 at DC and 1 at DR for Redundancy
	CPU	16 Cores		
 Agent Handler Connectivity	OS	Win Server 2025	2	Roaming client support (DC + DR)
	CPU	8 Cores		
 DLP Discover Storage Scan	HYP	VMware 6.7 / Nutanix	1	Optional for classification at DC
	CPU	16 Cores		

 NETWORK REQUIREMENTS

- ✓

Endpoint ↔ ePO Comm
- ✓

Firewall ↔ Skyhigh Cloud
- ✓

DNS Entries Configured
- ✓

ePO ↔ SQL Connectivity
- ✓

Public SSL Certificate
- ✓

Bandwidth Assessment

 O365 CASB PREREQUISITES

- License:

Microsoft 365 E3 or E5
- Role:

Global Admin for API integration
- Mailbox:

Auditing enabled for Exchange Online
- Audit:

Log Search enabled in Security & Compliance



CRITICAL SUCCESS FACTOR
Complete infrastructure validation (OS hardening, Network Access, HA failover) is mandatory before proceeding to solution deployment to reduce project risks.

Skyhigh Security Infrastructure

Virtual appliance and connector specifications

COMPONENT	SPECIFICATIONS			QTY	COMMENTS
 Virtual Appliance Web Gateway	HYP	VMware ESXi	RAM 32 GB	2	1 in DC and 1 in DR for Server traffic
	CPU	16 Cores	HDD 5 TB (Cache/Logs)		
 Database Server CSR Backend	OS	Win Server 2025/2022 Std	RAM 64 GB	2	High Availability (1 DC + 1 DR)
	CPU	8 Cores	HDD 500 GB (SQL 22/19/17)		
 Cloud Connector AD Sync	OS	Win Server 2025 Std	RAM 16 GB	2	Directory Synchronization
	CPU	8 Cores	HDD 500 GB		
 Cloud Connector SIEM Log Forwarding	OS	Win Server 2025 Std	RAM 16 GB	2	Secure Log Transport
	CPU	8 Cores	HDD 500 GB		




PRE-REQ TIMELINE

All infrastructure prerequisites must be fully provisioned and validated **before Week 1 kick-off** to ensure project schedule adherence.

Ref: Skyhigh Cloud Connector Prerequisites

16-Week Roadmap

📅 February - June 2026

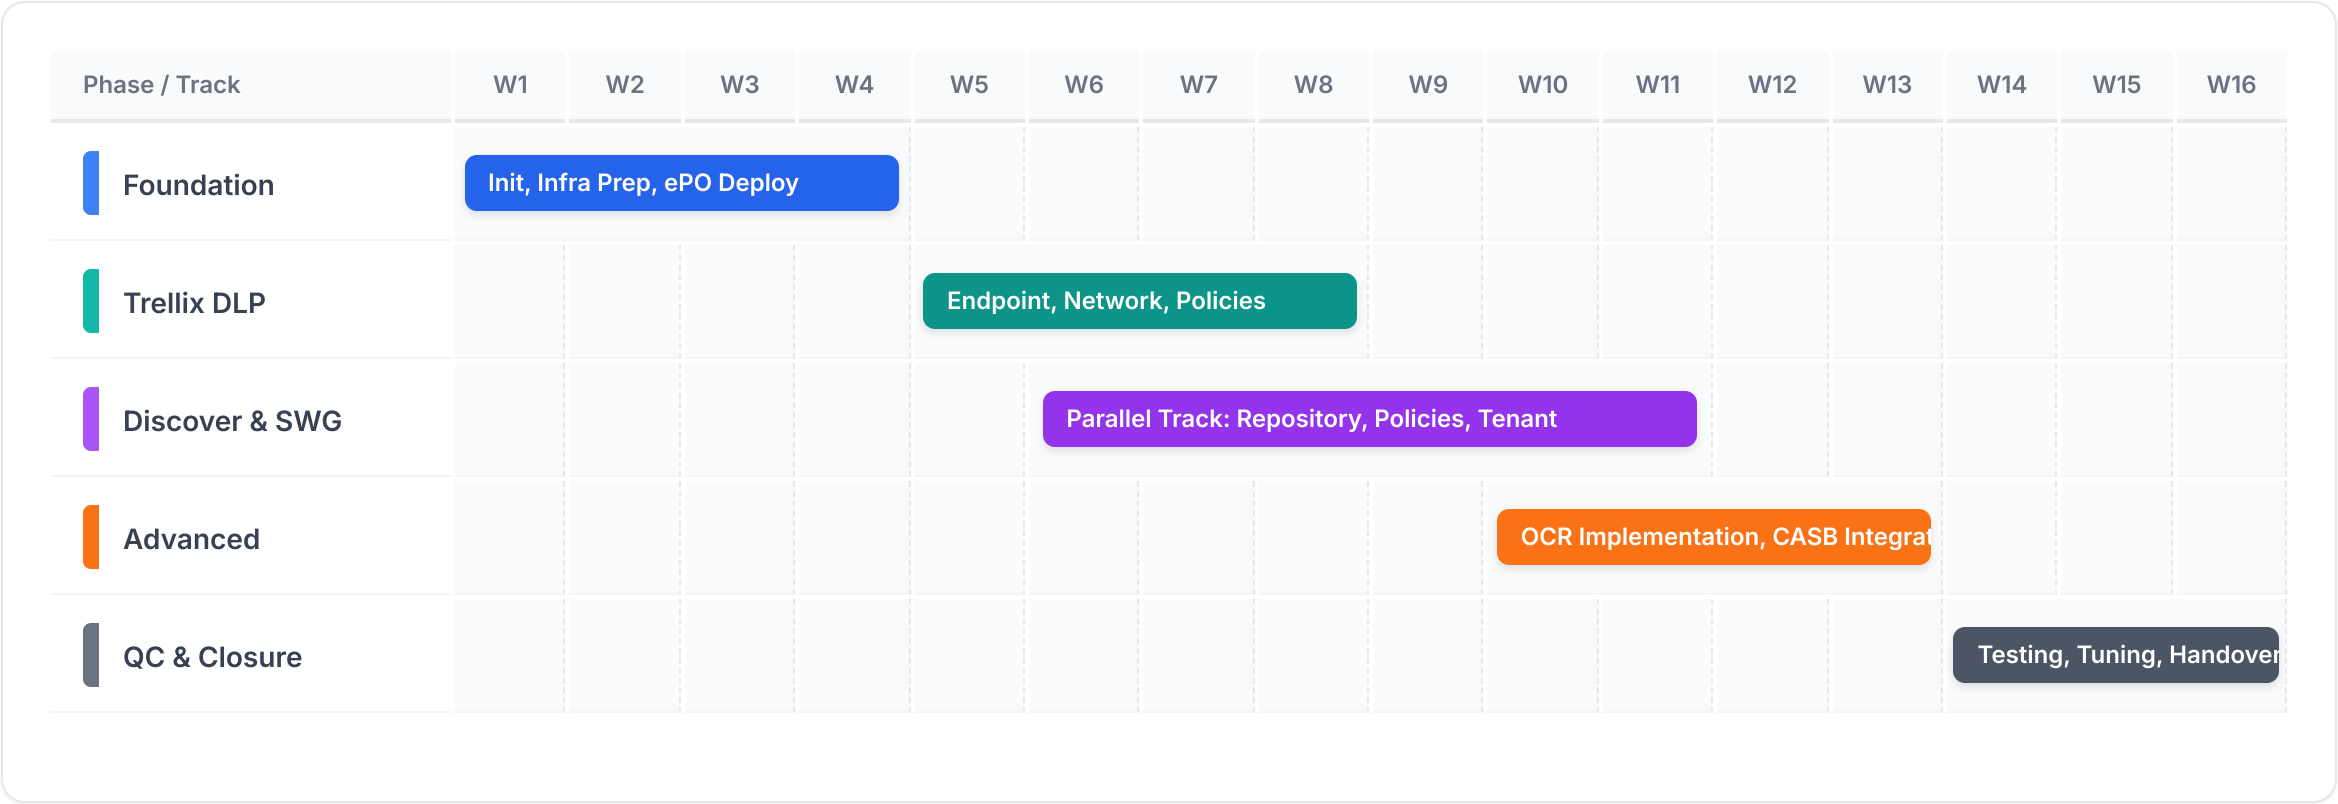

16
WEEKS DURATION



8
KEY PHASES



5
PARALLEL TRACKS



15+
DELIVERABLES

Foundation Setup

Weeks 1-4: Infrastructure Preparation & Core Deployment

WEEK 1

Project Initiation

- ✓ Kick-off meeting with all stakeholders
- ✓ Finalize project scope and boundaries
- ✓ Review and validate architecture design
- ✓ Define communication plan and cadence
- ✓ Create risk register and mitigation plans

DELIVERABLES

- Project Charter
- HLD Sign-off

WEEKS 2-3

Infrastructure Prep

- ✓ VM provisioning for all servers
- ✓ OS hardening and security baseline
- ✓ SQL Server installation & configuration
- ✓ High Availability (AlwaysOn) config
- ✓ Storage allocation and validation

DELIVERABLES

- Infra Readiness Report
- HA Validation

WEEK 4

ePO Deployment

- ✓ Install ePO Primary (DC)
- ✓ Install ePO Secondary (DR)
- ✓ Configure High Availability
- ✓ Install Agent Handler & AD sync
- ✓ Configure software repository

DELIVERABLES

- ePO Installation Doc
- HA Test Report



KEY SUCCESS FACTOR

Complete infrastructure validation before proceeding to solution deployment ensures all components are ready for seamless integration.

DLP Implementation & SWG Deployment

Weeks 5-11: Core Policy Design, Data Discovery & Cloud Security

WEEKS 5-8

Trellix DLP

✓ **Policy Design Workshop:** Define protection reqs & classification

✓ **Endpoint DLP:** USB control, File Copy, App Control, Email rules

✓ **DLP Prevent:** Network appliance, SMTP/HTTP integration

✓ **Rollout:** 50 Pilot → 1W Tuning → ≥95% Enterprise

✓ **Incident Workflow:** Automated alerting & routing setup

DELIVERABLES

DLP Policy Doc

Pilot Report

Rollout Report

WEEKS 6-11

DLP Discover

✓ **Repository Config:** CIFS, SMB, SharePoint, Databases, Box

✓ **Policy Creation:** Classification rules & discovery policies

✓ **Scan Execution:** Initial full scan & scheduled incrementals

✓ **Results Analysis:** Review incidents & validate accuracy

✓ **Tuning:** Refine policies to reduce false positives

DELIVERABLES

Workflow Config

Scan Reports

WEEKS 6-11

Skyhigh SWG

✓ **Setup:** Tenant provisioning, RBAC, Identity (SAML) integration

✓ **Traffic Steering:** Agent-based or GRE tunnel config

✓ **Controls:** SSL Inspection, URL Filtering, App Control

✓ **Protection:** Web DLP patterns & Anti-Malware

DELIVERABLES

SWG Policy Config

Web DLP Rules

CRITICAL SUCCESS FACTOR: MONITOR MODE FIRST

Begin DLP & Web DLP in observation mode before enforcement to minimize business disruption and validate policy accuracy.

Advanced Features

Weeks 10-13: Optical Character Recognition & CASB Integration



OCR Implementation

Image-to-Text Analysis Engine

SUPPORTED FORMATS

- GIF
- JPEG
- PNG
- PDF
- TIFF
- BMP

OPERATIONAL REQUIREMENTS

MIN CHARACTERS
25-30 per image

RESOLUTION
75 - 2400 dpi

MAX DIMENSIONS
8400 × 8400 px

TARGET ACCURACY
≥ 90%

**Global Coverage**
Multi-language support included for all major Western & Asian character sets.



CASB for O365

API-Based Cloud Protection

PREREQUISITES

Mandatory

- ✓

M365 E3 or E5 License
- ✓

Global Admin Role
- ✓

Exchange Auditing On
- ✓

Audit Log Search On

INTEGRATION WORKFLOW

- 1

Configure Secure Content Integrator in SharePoint Admin
- 2

Set up SharePoint API Integration & Grant Permissions
- 3

Configure OneDrive Integration
- 4

Integrate Exchange Online & Enable DLP Policies
- 5

Configure Teams Protection (Optional)

DLP AT REST/MOTION

INSIDER THREAT DETECTION

RACI Matrix

ACTIVITY / TASK	CUSTOMER	PARTNER (VINCA)	TRELLIX	SKYHIGH
Infrastructure Provisioning	R	C	I	I
SQL HA Setup	R	C	I	-
ePO Installation	I	R	C	-
DLP Policy Design	C	R	C	-
DLP Discover Configuration	C	R	C	-
SWG Policy Setup	C	R	-	C
SSL Certificate Deployment	R	C	I	I
Traffic Steering	R	R	-	C
OCR Configuration	C	R	-	C
CASB O365 Integration	R	R	-	C
DR Testing & Training	R	R	C	C

R

Responsible
Does the work

A

Accountable
Approver

C

Consulted
Provides input

I

Informed
Kept updated

Acceptance Criteria

Success Validation

Trellix Criteria

- ✓ ePO High Availability functional
- ✓ SQL Failover tested (AlwaysOn)
- ✓ DLP Endpoint ≥95% deployment
- ✓ DLP Prevent blocking policies
- ✓ DLP Discover scans operational
- ✓ SIEM log ingestion verified

Skyhigh SWG Criteria

- ✓ ≥95% Web Traffic steered to proxy
- ✓ SSL Inspection functioning
- ✓ URL Filtering categories validated
- ✓ Web DLP detection active
- ✓ Malware/Threat blocking confirmed

OCR & CASB Criteria

- ✓ OCR Text Extraction ≥90% accuracy
- ✓ O365 API Integration (SharePoint/OneDrive)
- ✓ Collaboration policies enforced
- ✓ External sharing restrictions

★ CRITICAL SUCCESS FACTORS

STRATEGY
Monitor Mode First

DEPLOYMENT
Certificate First

VALIDATION
Validate Pilot Group

CONFIGURATION
Align DLP Patterns

RESILIENCE
HA Failover Testing

Risk Management

Risk Matrix & Mitigation Strategies

⚠ Risk Analysis

IDENTIFIED RISKS

**False Positives**
User Disruption

HIGH

MITIGATION
Deploy policies in **monitor mode first** to tune accuracy.

**HA Misconfiguration**
Service Downtime

HIGH

MITIGATION
Perform comprehensive **DR testing** before go-live.

**SSL Inspection Issues**
App Breakage

MED

MITIGATION
Whitelist financial & incompatible sites.

**Roaming User Issues**
Policy Bypass

MED

MITIGATION
Thorough **agent validation testing** on off-net devices.

**OCR Performance**
Latency

MED

MITIGATION
Implement **file size limits** and type exclusions.

**CASB API Throttling**
Sync Delay

LOW

MITIGATION
Active **rate limit monitoring** & back-off.

MANDATORY DELIVERABLES

-  High-Level Design (HLD)
-  Low-Level Design (LLD)
-  Policy Matrix
-  HA Architecture Diagram
-  Traffic Steering Design
-  SSL Inspection SOP
-  Incident Workflow
-  DR Runbook

Partnership for **Success**

Vinca is committed to ensuring the long-term success of your Trellix DLP, Skyhigh SWG, and DLP Discover implementation.



Expert Team

Certified Engineers at your service



Always On

24/7 Support Coverage



Data-Driven

Quarterly Reviews & Insights



Protected

Your Security is Our Priority

Thank you for choosing us as your **security partner**
